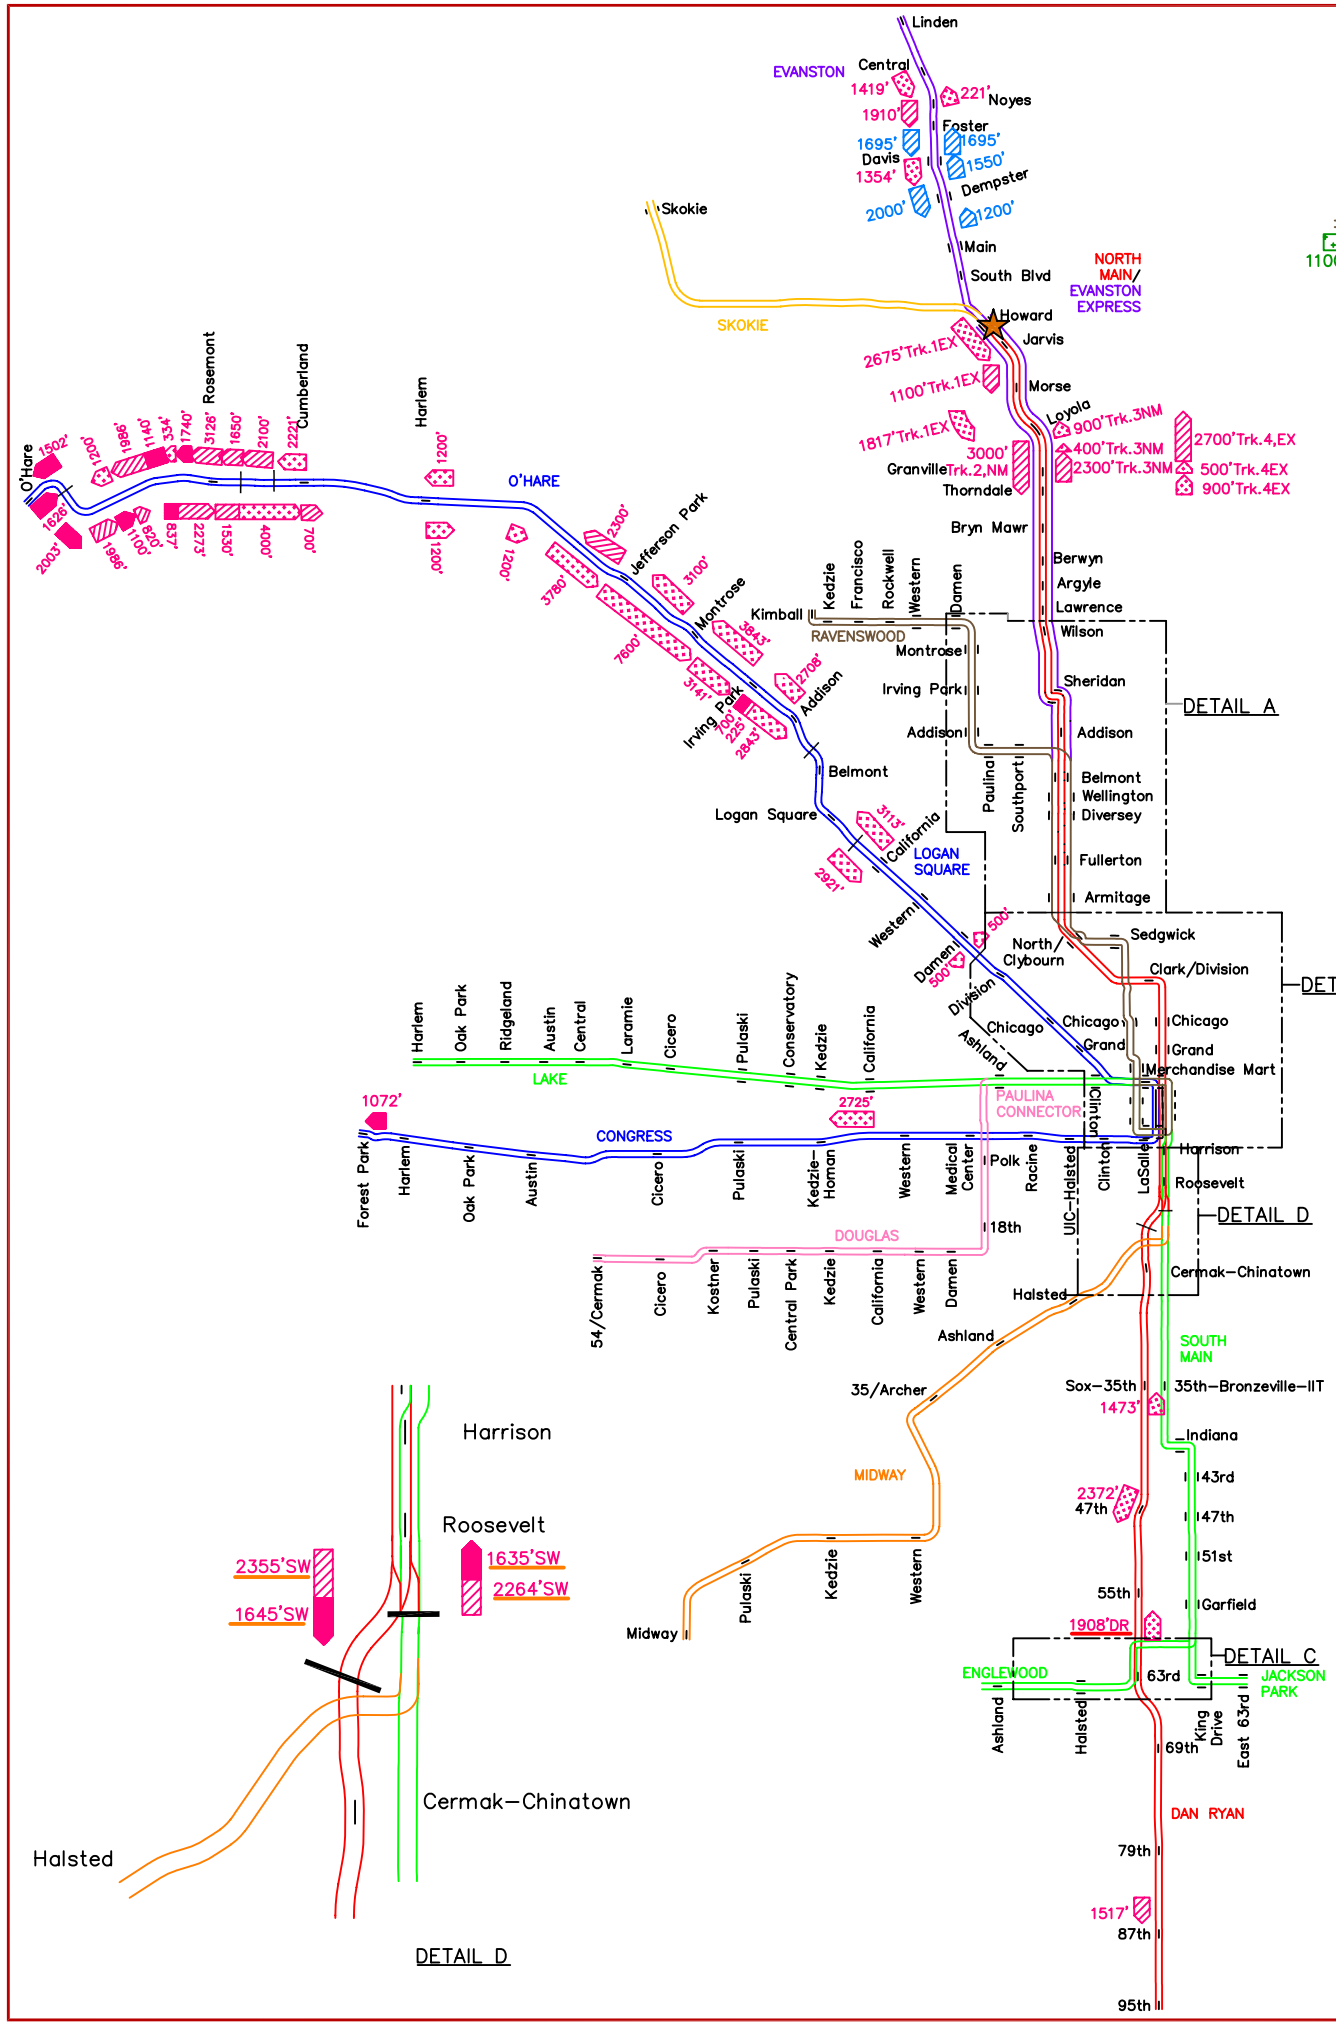

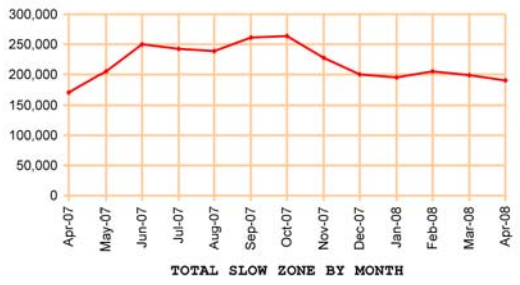

NOT TO SCALE
GRAPHICAL REPRESENTATION

SLOW ZONE BY AREA				
Track (CTA)	15 mph		28,439	150,200
	25 mph		46,577	
	35 mph		75,184	
Structure (CTA)	15 mph		0	8,140
	25 mph		8,140	
	35 mph		0	
Signal (CTA)	15 mph		0	0
	25 mph		0	
	35 mph		0	
Power (CTA)	15 mph		0	0
	25 mph		0	
	35 mph		0	
Construction (CTA/Contractor)	15 mph		16,152	26,138
	25 mph		1,724	
	35 mph		8,262	

★ NOTE: SIGNAL ISSUE RESULTING IN MULTIPLE 10 MIN. PLUS DELAYS DURING PREVIOUS MONTH

TOTAL SLOW ZONE TRACK

Rail Line	15 mph	25 mph	35 mph	Total Slow Zone	Linear Trk.–Ft.	% Slow	Movement Removed	Movement Added	Total SZ	% Slow
Congress	1,072	0	2,725	3,797	94,010	4.0	0	2,725		
O'Hare/Logan Square	10,648	19,258	45,404	75,310	152,956	49.2	6,771	1,200	79,107	27.0
Dearborn Subway	0	0	0	0	45,818	0	0	0		
North Main Line	2,600	7,580	900	11,080	78,966	14.0	0	0		
State Subway	16,152	6,104	3,442	25,698	51,328	50.1	0	0	44,048	19.0
Dan Ryan	0	1,517	5,753	7,270	101,332	7.2	0	1,473		
Skokie	0	0	0	0	52,146	0	0	0	0	0
Evanston	0	10,050	2,994	13,044	40,714	32.0	0	0	30,411	29.9
Evanston Express	4,962	5,113	7,292	17,367	60,970	28.5	900	900		
Loop	556	0	0	556	21,470	2.6	0	0	556	2.6
Ravenswood/Ravenswood–Loop	4,071	2,200	7,262	13,533	98,364	13.8	8,900	7,262	13,533	13.8
Midway/Grand Junction	3,280	4,619	0	7,899	99,224	8.0	0	0	7,899	8.0
Lake	0	0	0	0	93,114	0	0	0		
South Loop/South Main Line	0	0	0	0	68,906	0	0	0	8,924	4.3
Englewood	1,250	0	7,674	8,924	31,916	28.0	200	200		
Jackson Park	0	0	0	0	12,162	0	0	0		
Douglas/Paulina Connector	0	0	0	0	77,710	0	0	0	0	0.0
TOTALS	44,591	56,441	83,446	184,478	1,181,106	15.6	16,771	13,760		

DATE	DESCRIPTION	
		IN CHARGE C.B.
		APPROVED BY B.M.jr
		CHECKED BY B.M.jr
		UPDATED BY S.M.
16 MAY 06	ORIGINAL	ORIGINATED BY J.J.H.
		Prepared by: Track Maintenance

CTA RAIL CUSTOMER IMPACT MAP

April 30, 2008
